BRHAT BANGALORE MAHANAGARA PALIKE

INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Providing Street lights and electrical connection in Ward no 12 Shettyhalli Sub Division	
2	Estimate Cost	5.00 Lakhs	
3	Administrative Approved No and Date	BBMP/EE/DD/AS/49/15-16 Date. 04.01.2016.	
4	Technical sanction No. and Date	BBMP/EE/DD/TS(E)/01/15-16 Date. 05.01.2016.	
5	Job Code No. and P Code No.	012-16-000012	
6	Tender Direct Entrested to KRIDL	Not Applicable	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	BBMP/EE/DD/TEN/01/2016-17, Dated:21.04.2016	
8	Tender Approved Details	CE Approval Dated:04.01.2016.	
9	Work Order No and Date	EE/ELE/DD/WO/23/2016-17, Dt:23.05.2016.	
10	Stipulation time of Completion	90 Days	
11	Actiual Date of Commencement	24.05.2016	
12	Actiual Date of Completion	22.08.2016	
13	Delay if any	Nil	
14	Reson for Delay	Nil	

Executive Engineer (Ele)
Bruhath Bangalore Mahanagara Palike
Dasarahalli Zone

15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	19-12-2016	
19	MB No. and Page No.	MB No. 5121 Page No. 512021 to 512035	
20	BR No. and Date	15/16-17 Dated:25/06/2016	
21	Section officer	Sri Babu Reddy.K.N J.E	
22	Sub Division Officer	Sri. K.Nagesh. AEE	
23	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	

Executive Engineer (Ele)
Bruhath Bangalore Mahanagara Palike
Dasarahalli Zone

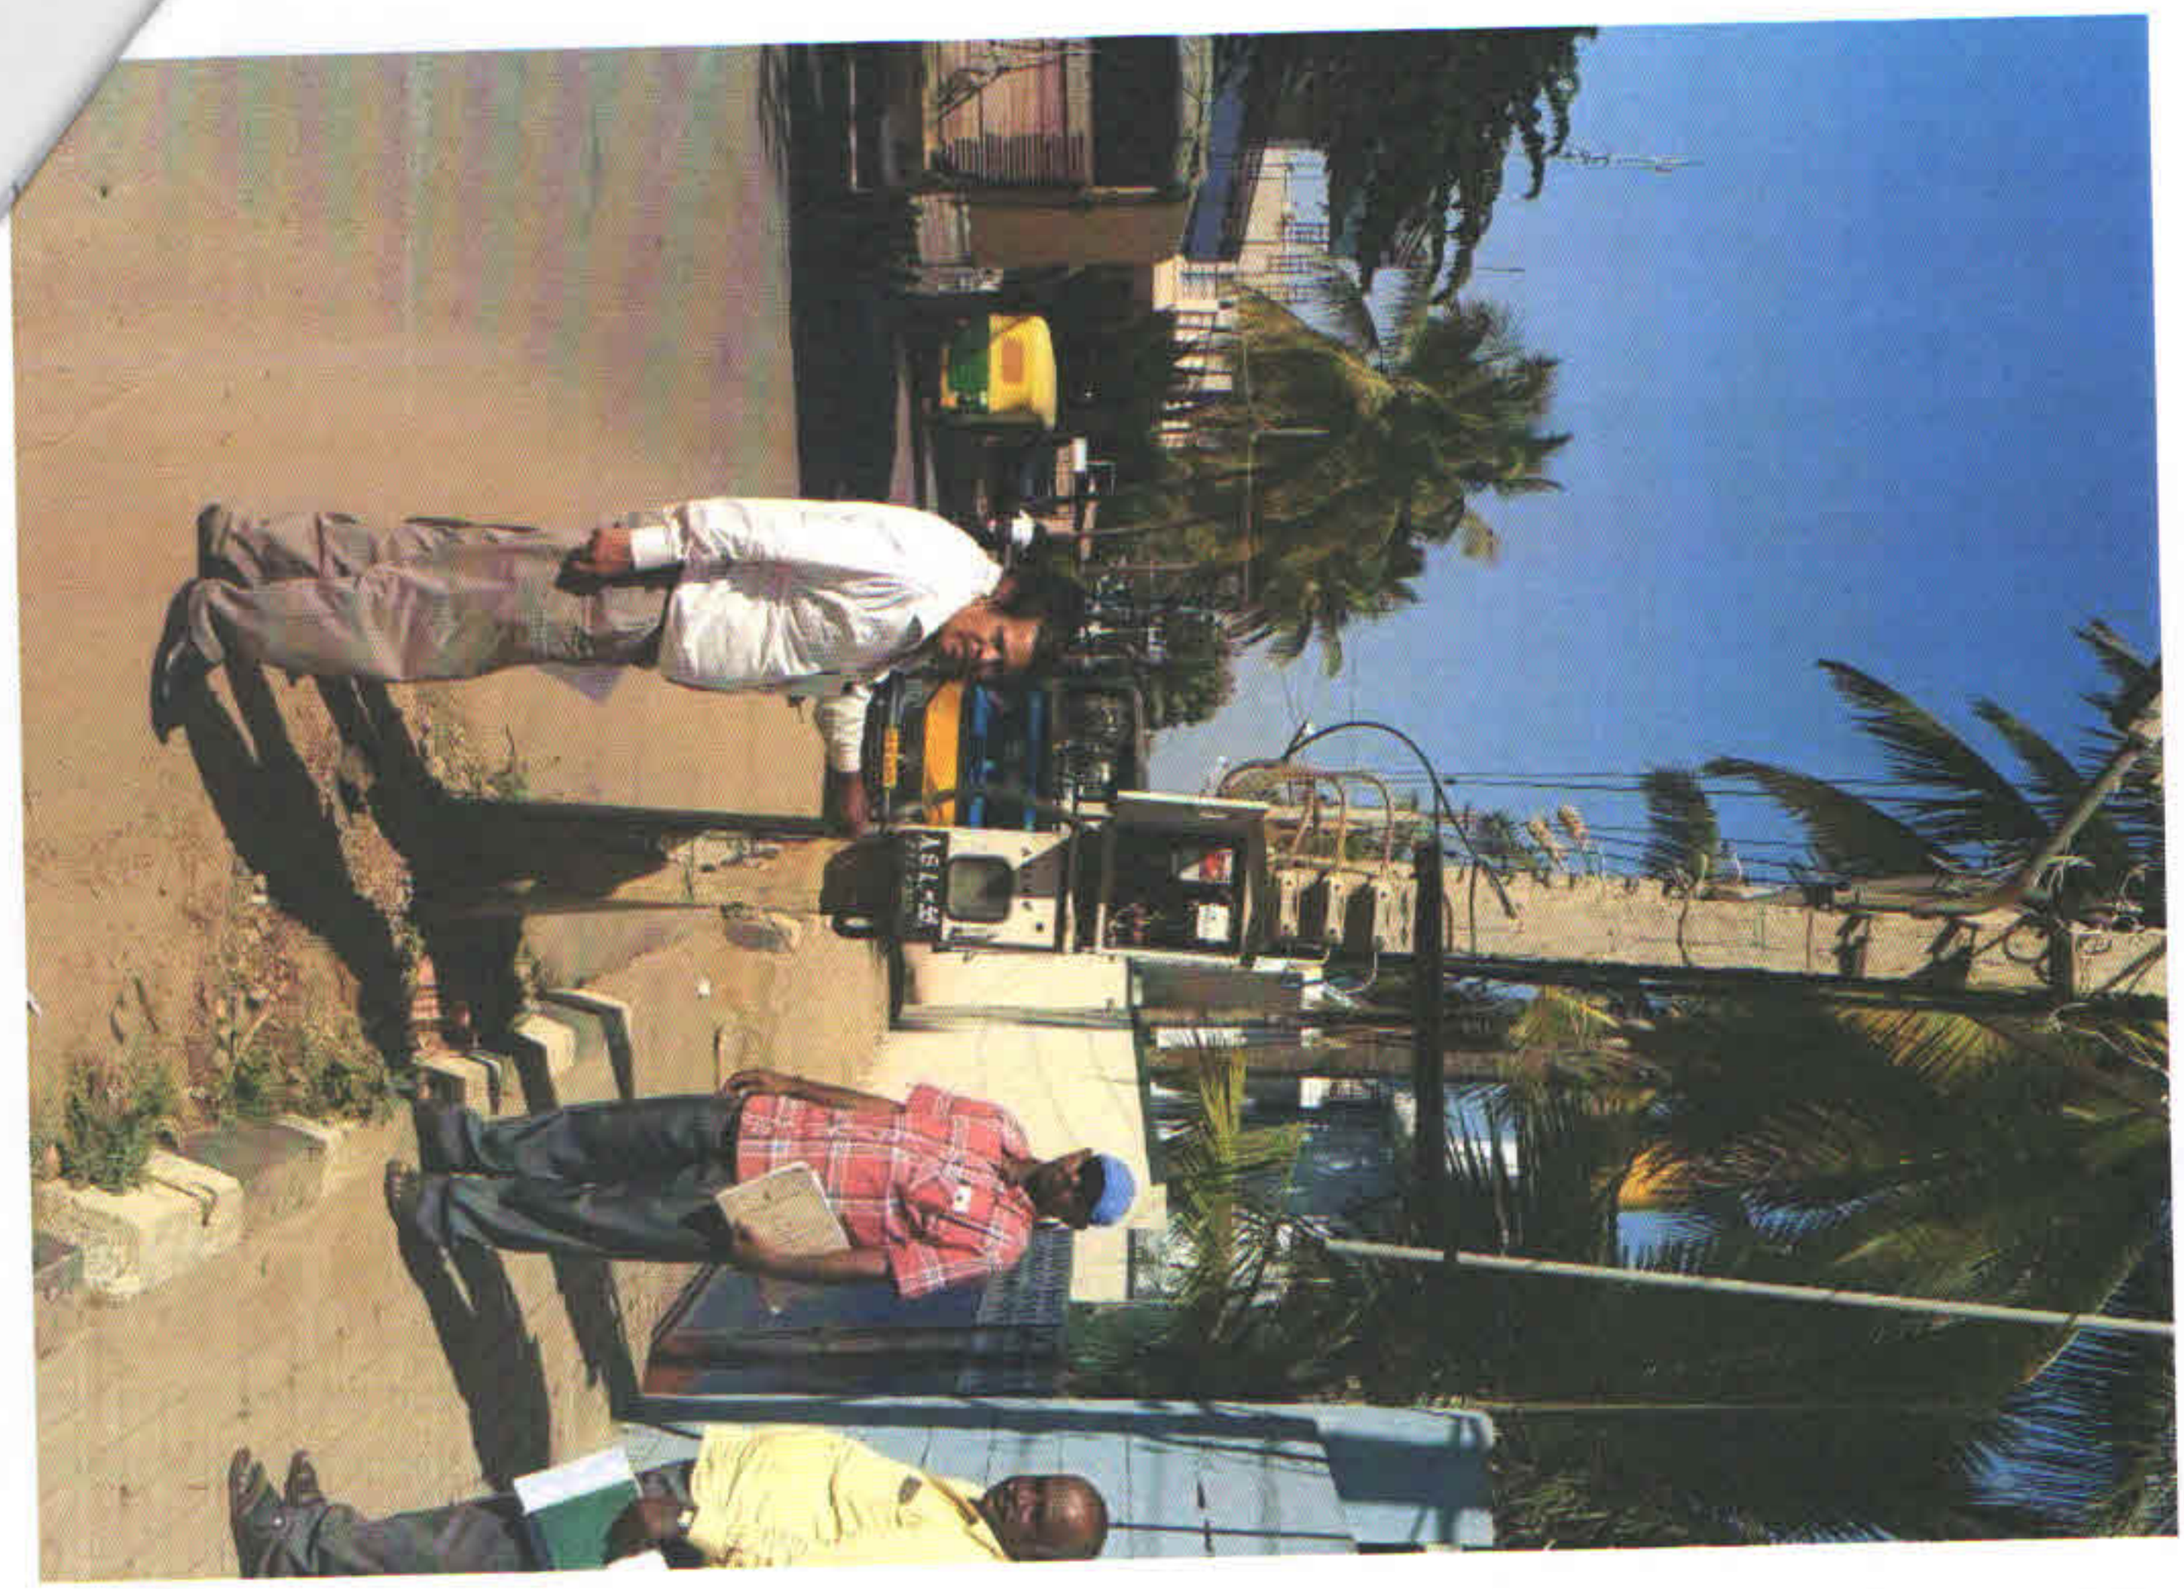

Executive Engineer (Ele)
Bruhath Bangalore Mahanagara Palike
Dasarahalli Zone
